

<b>PROJECT:</b>	Wells County Public Library Renovations	<b>SUPPLEMENTAL INFORMATION (SI) NUMBER:</b>	<b>15.2</b>
		<b>DATE OF ISSUE:</b>	5/5/2020
<b>OWNER:</b>	WCPL	<b>CONTRACT FOR:</b>	General Construction
		<b>CONTRACT DATED:</b>	12/9/2019
<b>TO CONTRACTOR:</b>	CME Corporation	<b>ARCHITECT'S PROJECT NUMBER:</b>	19067

Submit proposal or proceed with the Work as indicated below:

- ☒ Supplemental information issued as PROPOSAL REQUEST: Please submit an itemized proposal for changes in the Contract Sum and Contract Time for proposed modifications to the Contract Documents described herein. THIS IS NOT A CHANGE ORDER, A CONSTRUCTION CHANGE DIRECTIVE OR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED IN THE PROPOSED MODIFICATIONS. Contractor to receive written approval by the Architect prior to commencing work.
- ☐ *SUPPLEMENTAL INSTRUCTIONS shall be carried out in accordance with the modifications to the Contract Documents described herein issued in accordance with Contract Documents without change in Contract Sum or Contract Time. Proceeding with the Work in accordance with these instructions indicates your acknowledgement that there will be no change in the Contract Sum or Contract Time.*
- ☐ *The Work described in the supplemental information to be performed on a "TIME AND MATERIALS" (T&M) basis. Contractor to receive written approval by the Owner for the scope of work described herein prior to commencing work.*

**SUMMARY:** New Lighting in rooms 128, 129 and 147  
**DESCRIPTION:**

Contractor to provide price and cost breakdown for owner approval prior to proceeding.

Contractor to provide the cost for the demolition of lighting in Children's Collection Room 147, Teen Lounge Room 129, and Collection Room 128 as shown on attached documents.

Contractor to provide the cost for the addition of new fixtures specified in Children's Room 147, Teen Lounge Room 129, and Collection Room 128 as shown on attached documents. Contractor to provide all hardware, accessories, conduit and conductors for a complete and code compliant system.

Contractor to provide separate breakout costs for:

1. New lighting work shown on E201-04-06-2020a - within the designated boundary
2. New lighting work shown on E201-04-06-2020b - within the designated boundary

**AREA #1: \$36,407.06 (SEE PCO #043 ATTACHED)**

**AREA #2: \$42,910.36 (SEE PCO #044 ATTACHED) INCLUDES NEW FIXTURES IN 127**

**TOTAL: \$79,317.42**

**ATTACHMENTS:** ESI #11 R1, SI 15.1 (ANNOTATED WITH DESIGNATED BOUNDARIES)  
**ISSUED BY:** Andrew Hesterman  
**CC:** WCPL, CME, SCO

<b>PROJECT:</b>	Wells County Public Library Renovations	<b>SUPPLEMENTAL INFORMATION (SI) NUMBER:</b>	<b>15.1</b>
		<b>DATE OF ISSUE:</b>	4/8/2020
<b>OWNER:</b>	WCPL	<b>CONTRACT FOR:</b>	General Construction
		<b>CONTRACT DATED:</b>	12/9/2019
<b>TO CONTRACTOR:</b>	CME Corporation	<b>ARCHITECT'S PROJECT NUMBER:</b>	19067

Submit proposal or proceed with the Work as indicated below:

- ☒ Supplemental information issued as PROPOSAL REQUEST: Please submit an itemized proposal for changes in the Contract Sum and Contract Time for proposed modifications to the Contract Documents described herein. THIS IS NOT A CHANGE ORDER, A CONSTRUCTION CHANGE DIRECTIVE OR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED IN THE PROPOSED MODIFICATIONS. Contractor to receive written approval by the Architect prior to commencing work.
- ☐ *SUPPLEMENTAL INSTRUCTIONS shall be carried out in accordance with the modifications to the Contract Documents described herein issued in accordance with Contract Documents without change in Contract Sum or Contract Time. Proceeding with the Work in accordance with these instructions indicates your acknowledgement that there will be no change in the Contract Sum or Contract Time.*
- ☐ *The Work described in the supplemental information to be performed on a "TIME AND MATERIALS" (T&M) basis. Contactor to receive written approval by the Owner for the scope of work described herein prior to commencing work.*

**SUMMARY:** New Lighting in rooms 128, 129 and 147  
**DESCRIPTION:**

Contractor to provide price and cost breakdown for owner approval prior to proceeding.

Contractor to provide the cost for the demolition of lighting in Children's Collection Room 147, Teen Lounge Room 129, and Collection Room 128 as shown on attached documents.

Contractor to provide the cost for the addition of new fixtures specified in Children's Room 147, Teen Lounge Room 129, and Collection Room 128 as shown on attached documents. Contractor to provide all hardware, accessories, conduit and conductors for a complete and code compliant system.

**ATTACHMENTS:** ESI #11 R1  
**ISSUED BY:** Craig Campbell  
**CC:** WCPL, CME, Andrew Hesterman

***Engineering Supplemental Information***

*6534 Constitution Drive  
Fort Wayne, IN 46804  
(260) 436-9213  
fax (260) 432-5481*

ENGINEER'S SUPPLEMENTAL INSTRUCTIONS #11R1  
Wells County Public Library Renovation  
200 West Washington Street  
Bluffton, IN 46714  
Commission No. 192414

April 6, 2020

- Item No. 1:** On sheet E-001, the electrical contractor shall state the cost for the demolition of lighting in Childrens Collection Room #147, Teen Lounge Room #129, and Collection Room #128 as shown on attached Supplemental Information Drawing 2414E001-03-25-2020-SI-15.
- Item No. 2:** On sheet E-201, the electrical contractor shall state the cost for the addition of new fixtures specified in Childrens Collection Room #147, Teen Lounge Room #129, and Collection Room #128 as shown on attached Supplemental Information Drawing 2414E201-03-25-2020-SI-15R1a, 2414E201-03-25-2020-SI-15R1b, and 2414E201-03-25-2020-SI-15R1c. Contractor provide all hardware, accessories, conduit, and conductors for a complete and code compliant system.



EXISTING FIRE ALARM DEVICES SHALL BE REMOVED ALONG WITH ASSOCIATED CONDUIT, RACEWAYS, AND CONDUCTORS. PROVIDE AND INSTALL A CUSTOM-CUT OVERSIZED STAINLESS STEEL BLANK COVER WHERE WALL MOUNTED DEVICES ARE REMOVED THAT IS LARGER THAN REMOVED DEVICE, SO EXISTING FINISH APPEARS UNDISTURBED. PROVIDE AND INSTALL NEW CEILING TILE THAT MATCHES ADJACENT WHERE CEILING MOUNTED DEVICES ARE REMOVED, OR PATCH AND PAINT HARD CEILINGS TO MATCH ADJACENT SURFACE.

WHERE EXISTING PANELS AND DEVICES ARE REMOVED FROM EXISTING WALLS, AND NO NEW PANEL OR DEVICE IS INDICATED AS A REPLACEMENT, EXISTING LOCATION SHALL BE PATCHED WITH LIKE MATERIAL, TEXTURE, COLOR, ETC. RESTORATION SHALL MATCH ADJACENT SURFACE.

EXISTING ELECTRICAL DEVICES BEING REMOVED IN EXISTING WALLS TO REMAIN SHALL HAVE ALL ASSOCIATED CONDUIT AND CONDUCTORS REMOVED BACK TO RESPECTIVE PANELBOARD. ELECTRICAL CONTRACTOR SHALL COORDINATE WITH GENERAL CONTRACTOR FOR PATCHING OF WALL TO MATCH ADJACENT SURFACES, TYPICAL.


- ### ELECTRICAL DEMOLITION PLAN NOTES
- DISCONNECT MECHANICAL EQUIPMENT FOR REMOVAL BY MECHANICAL CONTRACTOR, ASSOCIATED CONDUIT AND CONDUCTORS SHALL BE REMOVED IN THEIR ENTIRETY TO POINT OF ORIGIN.
  - ELECTRICAL CONTRACTOR SHALL DISCONNECT AND REMOVE EXISTING FIBER OPTIC LIGHTING SYSTEM IN THIS AREA.
  - ELECTRICAL CONTRACTOR SHALL DISCONNECT LENGTH OF SECTIONS SHOWN. CONTRACTOR SHALL KEEP END CAP OF FIXTURE RUN FOR REINSTALLATION. REFER TO SHEET E-201 FOR ADDITIONAL INFORMATION.
  - ELECTRICAL CONTRACTOR SHALL REMOVE REMOTE BALLASTS ASSOCIATED WITH MAIN LOBBY PENDENT LIGHTING LOCATED ON THE MEZZANINE CATWALK. CONTRACTOR SHALL REMOVE ALL CONDUIT AND CONDUCTORS BACK TO THE POINT OF ORIGIN.
  - BASE BID: NO WORK IN THIS AREA.
  - ALTERNATE BID: CONTRACTOR SHALL DEMOLISH ELECTRICAL DEVICES AS SHOWN. PREPARE EXISTING CONDUCTORS FOR NEW WORK AS NECESSARY.
  - CONTRACTOR SHALL DISCONNECT AND REMOVE CEILING MOUNTED RECEPTACLE AND REMOVE CONDUCTORS BACK TO EXISTING JUNCTION BOX ABOVE CEILING AND PREPARE CONDUCTORS FOR NEW WORK.
  - ELECTRICAL CONTRACTOR SHALL DISCONNECT AND REMOVE EXISTING RECEPTABLES AND PREPARE CONDUCTORS AND JUNCTION BOX FOR NEW WORK.

### GENERAL CONDITIONS NOTE

ALL CONTRACTORS, BY MAKING THEIR BID, REPRESENT THAT THEY HAVE READ AND UNDERSTAND THE CONSTRUCTION DOCUMENTS. THE CONTRACTOR SHALL REFER TO THE ENTIRE CONSTRUCTION DOCUMENT SET FOR GUIDANCE ON DIMENSIONS, HEIGHTS, DETAILING, ETC. AND INSTALL THEIR WORK SO AS NOT TO INTERFERE WITH THE INSTALLATION OF ANOTHER DISCIPLINE'S WORK OR THE GENERAL INTENT OF THE CONSTRUCTION DOCUMENTS. IN THE EVENT OF A CONFLICT BETWEEN THE SPECIFICATIONS AND/OR DRAWINGS, THE ARCHITECT SHALL DETERMINE WHICH INFORMATION GOVERNS.

M/P/E TRADES NOTE: IN REFERRING TO THIS SHEET YOU ACKNOWLEDGE:

- REVIEWING THE ENTIRE DRAWING SET INCLUDING ALL 'S', 'C' & 'M' SERIES.
- COORDINATING WITH THE GENERAL TRADES CONTRACTOR OR G.M. FOR EXACT DETAILING, HEIGHTS, ETC. PRIOR TO INSTALLING WORK.

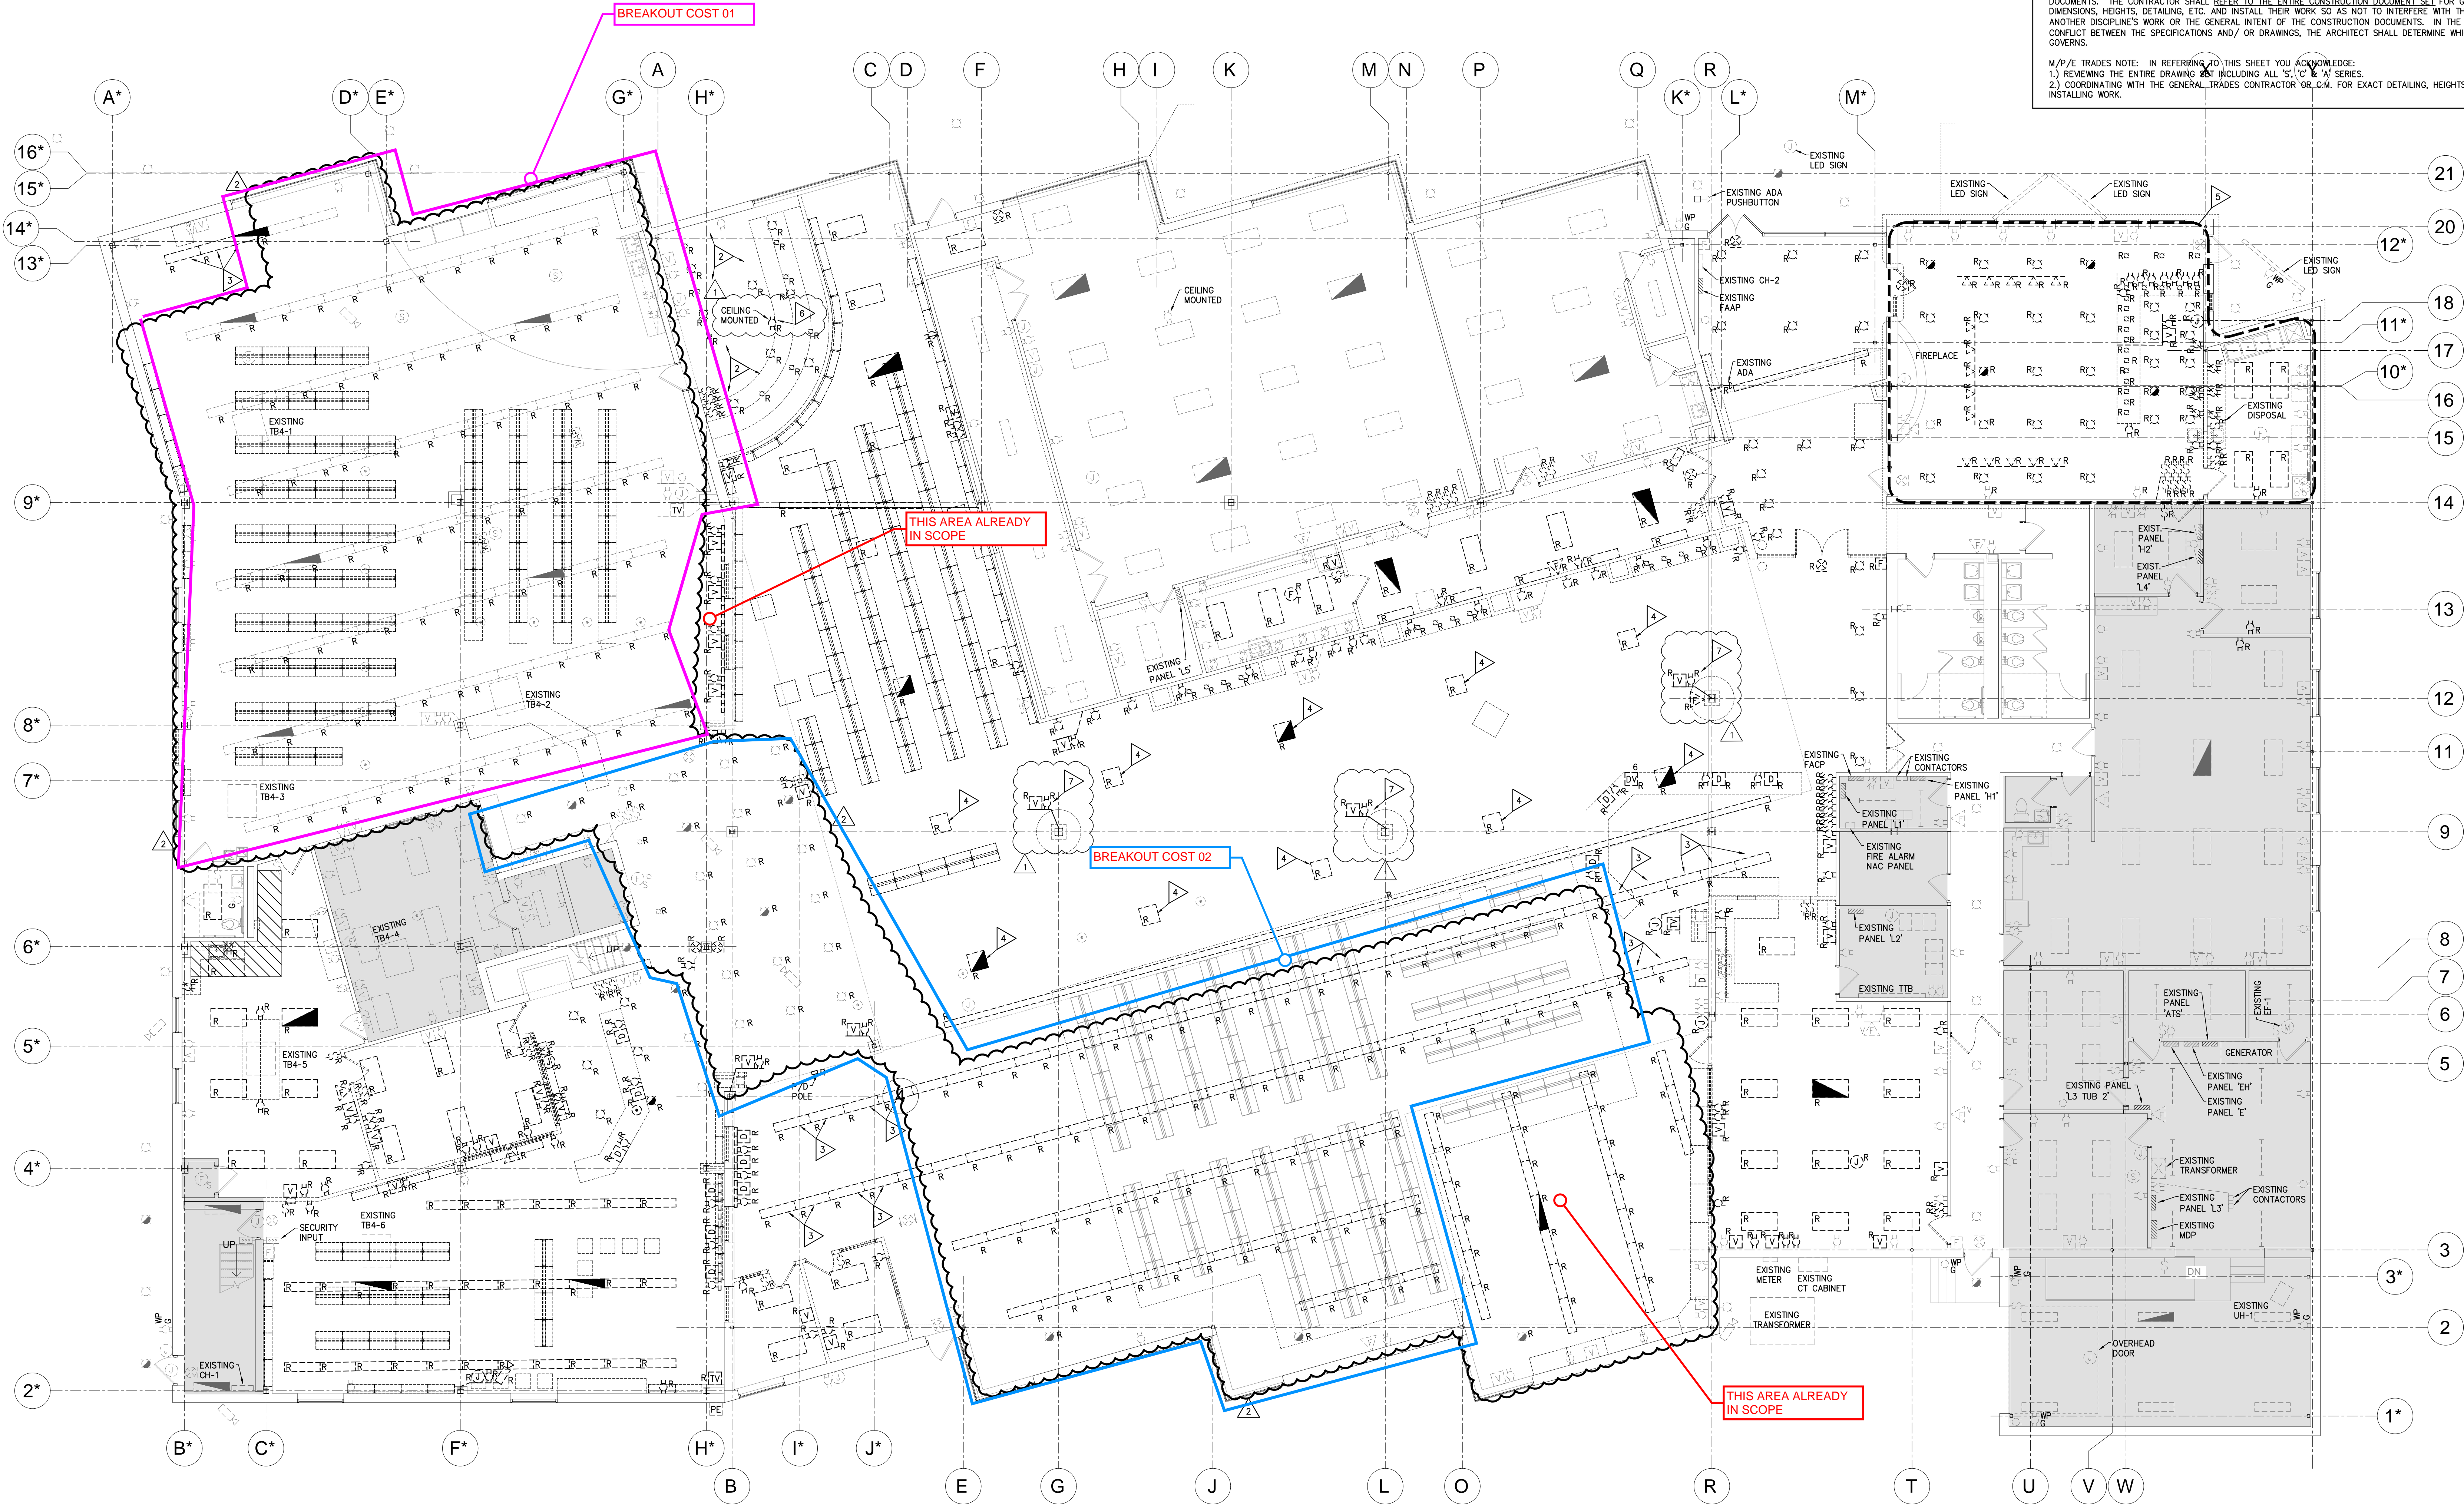

**FIRST FLOOR ELECTRICAL DEMOLITION PLAN**

2' 4' 8' 16' 32'

SCALE

**MKM**  
architecture + design

119 West Wayne Street  
Fort Wayne, Indiana 46802  
P 260.422.0783  
www.MKMdesign.com

Certification:  
THOMAS P. O'LEARY  
REGISTERED  
No. 10303150  
STATE OF INDIANA  
PROFESSIONAL ENGINEER  
Contract Logo  
SCO ENGINEERING LLC  
119 West Wayne Street  
Fort Wayne, Indiana 46802  
P 260.422.0783  
www.MKMdesign.com

This is an original design, created by SCO ENGINEERING LLC. The contents, ideas, plans and details are the sole property of SCO ENGINEERING LLC. No part of this drawing shall be reproduced or used in any manner without the written permission of SCO ENGINEERING LLC. This drawing shall be used only for the project and location specified herein. Any other use of this drawing without the written permission of SCO ENGINEERING LLC is prohibited. The user of this drawing shall be responsible for all dimensions and conditions shown on this drawing and shall be responsible for all dimensions and conditions shown on this drawing and shall be responsible for all dimensions and conditions shown on this drawing.

Key Plan:

ALL IDEAS, DESIGNS, ARRANGEMENTS AND PLANS INDICATED BY THIS DRAWING ARE OWNED BY AND THE PROPERTY OF MKM ARCHITECTURE + DESIGN. AND WERE CREATED AND DEVELOPED FOR USE ON, AND IN CONNECTION WITH THIS SPECIFIC PROJECT. NO PART OF THIS DRAWING SHALL BE REPRODUCED OR USED IN ANY MANNER WITHOUT THE WRITTEN PERMISSION OF MKM ARCHITECTURE + DESIGN. THE OWNER SHALL BE PERMITTED TO RETAIN COPIES FOR INFORMATION AND REFERENCE IN CONNECTION WITH THE PROJECT. ANY OTHER USE OR NOT SHOWN ON THIS DOCUMENT, WHICH VIOLATES THE WRITTEN PERMISSION OF MKM ARCHITECTURE + DESIGN, SHALL BE CONSIDERED A VIOLATION OF THE TERMS OF THIS AGREEMENT. THE USER OF THIS DRAWING SHALL BE RESPONSIBLE FOR ALL DIMENSIONS AND CONDITIONS SHOWN ON THIS DRAWING AND SHALL BE RESPONSIBLE FOR ALL DIMENSIONS AND CONDITIONS SHOWN ON THIS DRAWING AND SHALL BE RESPONSIBLE FOR ALL DIMENSIONS AND CONDITIONS SHOWN ON THIS DRAWING.



**WELLS COUNTY PUBLIC LIBRARY RENOVATION**  
200 W. WASHINGTON ST.  
BLUFFTON, IN 46714

REVISION		
No.	Date	Revision
1	10.10.2019	ADD-01
2	10.25.2019	ADD-02
3	03.25.2020	ESI #11

DRAWING CONTENTS:  
FIRST FLOOR  
ELECTRICAL  
DEMOLITION PLAN


ISSUE DATE: 10.10.2019 PROJECT NO: 19067 (192414)

DRAWING NO.







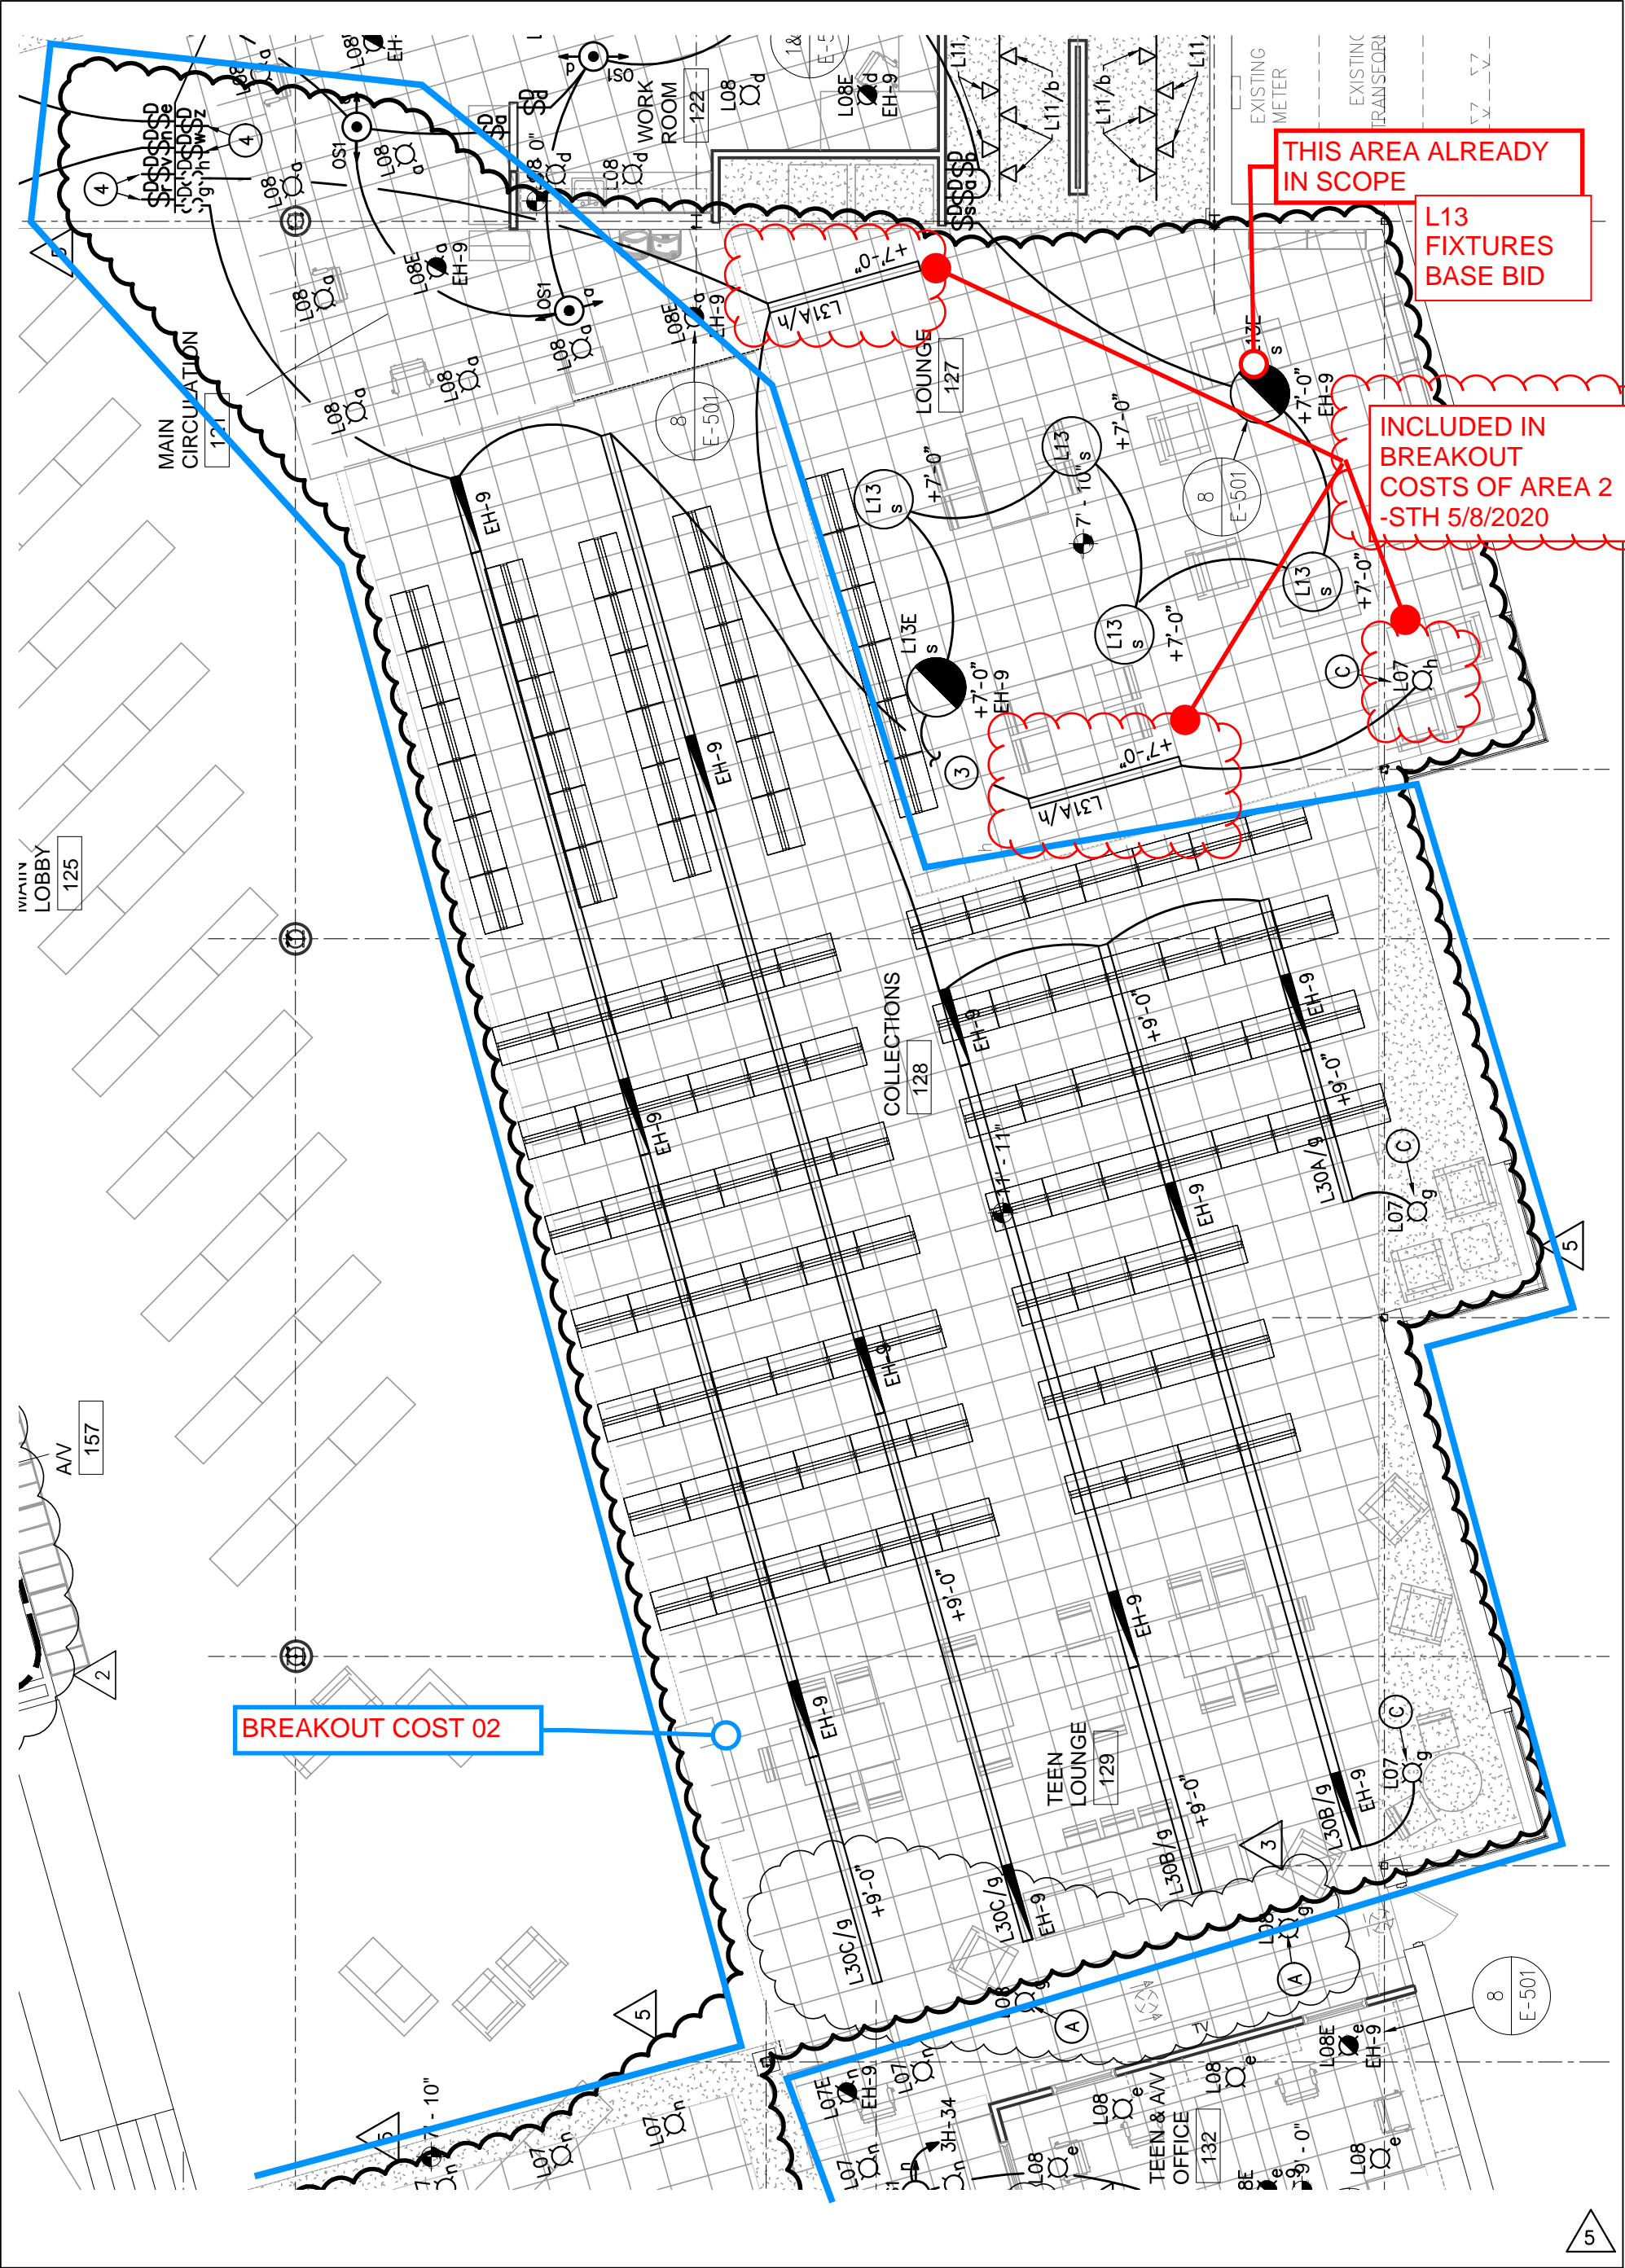

## ELECTRICAL PLAN NOTES

C ELECTRICAL CONTRACTOR SHALL PROVIDE GOOF RING FOR INSTALLATION OF NEW 'L07' FIXTURE IN EXISTING OPENING AS REQUIRED FOR COMPLETE INSTALLATION.

D ELECTRICAL CONTRACTOR SHALL TERMINATE NEW LIGHTING FIXTURES TO EXISTING CIRCUIT SERVING AREA. CONTRACTOR SHALL REPLACE EXISTING LIGHTING CONTROLS WITH NEW TO MAINTAIN EXISTING LIGHTING CONTROL CAPABILITY.

## LUMINAIRE SCHEDULE (SI-15)

TYPE	MANUFACTURER'S CATALOG NUMBER	MOUNT	LED		VOLTAGE	INPUT WATTS
			LUMENS	COLOR		
L30A	LITHONIA #GRAD-LLP-16FT-MSL8-80CRI-35K-ID1300LMF-80/20 -MIN10-ZT-277-SCT-1EC-F1/48A-C210-DU-MCS	PENDENT	4987 PER 4FT SECTION	35K	277	160
L30B	LITHONIA #GRAD-LLP-48FT-MSL8-80CRI-35K-ID1300LMF-80/20 -MIN10-ZT-277-SCT-2EC-F1/48A-C210-DU-MCS	PENDENT	4987 PER 4FT SECTION	35K	277	480
L30C	LITHONIA #GRAD-LLP-80FT-MSL8-80CRI-35K-ID1300LMF-80/20 -MIN10-ZT-277-SCT-3EC-F1/48A-C210-DU-MCS	PENDENT	4987 PER 4FT SECTION	35K	277	800
L31	LITHONIA #BLT4-20L-ADP-GZ10-LP835	GRID	1907	35K	277	16
L31E	LITHONIA #BLT4-20L-ADP-GZ10-LP835-EL14LSD	GRID	1907	35K	277	16

CME Corporation  
7235 Vicksburg Pike  
Fort Wayne, 46804  
Phone: (260) 745-0251

**Project:** 19218 - Wells County Public Library Interior Renovation  
200 W Washington St  
Bluffton, Indiana 46714

## Prime Contract Potential Change Order #043: CE #094 - SI-15.2 - New Lighting Area 1 OF 2

<b>TO:</b>	Wells County Public Library 200 W Washington Street Bluffton Indiana, 46714	<b>FROM:</b>	CME Corporation 7235 Vicksburg Pike Fort Wayne Indiana, 46804
<b>PCO NUMBER/REVISION:</b>	043 / 0	<b>CONTRACT:</b>	1 - Wells County Public Library Interior Renovation
<b>REQUEST RECEIVED FROM:</b>	Andrew Hesterman (MKM architecture + design)	<b>CREATED BY:</b>	Sean Hayes (CME Corporation)
<b>STATUS:</b>	Pending - In Review	<b>CREATED DATE:</b>	5/8 /2020
<b>REFERENCE:</b>		<b>PRIME CONTRACT CHANGE ORDER:</b>	None
<b>FIELD CHANGE:</b>	Yes		
<b>LOCATION:</b>	147/148	<b>ACCOUNTING METHOD:</b>	Amount Based
<b>SCHEDULE IMPACT:</b>		<b>PAID IN FULL:</b>	No
		<b>TOTAL AMOUNT:</b>	\$36,407.06

**POTENTIAL CHANGE ORDER TITLE:** CE #094 - SI-15.2 - New Lighting Area 1 OF 2

**CHANGE REASON:** Client Request

**POTENTIAL CHANGE ORDER DESCRIPTION:** (The Contract Is Changed As Follows)

CE #094 - SI-15.2 - New Lighting Area 1 OF 2

See attached SI-15.2 - New Lighting in rooms 147/148. - **AREA 1 OF 2**

Item No. 1: On sheet E-001, the electrical contractor shall state the cost for the demolition of lighting in Children's Collection Room #147, Teen Lounge Room #129, and Collection Room #128 as shown on attached Supplemental Information Drawing 2414E001-03-25-2020-SI-15.

Item No. 2: On sheet E-201, the electrical contractor shall state the cost for the addition of new fixtures specified in Children's Collection Room #147, Teen Lounge Room #129, and Collection Room #128 as shown on attached Supplemental Information Drawing 2414E201-03-25-2020-SI-15R1a, 2414E201-03-25-2020-SI-15R1b, and 2414E201-03-25-2020-SI-15R1c. Contractor provide all hardware, accessories, conduit, and conductors for a complete and code compliant system.

### ATTACHMENTS:

[INM PR - SI 15 2.pdf](#) [\\_Rosema Revised SI-15.1 Proposal.pdf](#) [\\_2020-05-05\\_SI-15.2 - New Lighting - Breakdown Designations.pdf](#)

#	Cost Code	Description	Type	Amount
1	16-16050 - Basic Electrical Materials	INM - SI-15.2-Area 1 - New Lighting	Commitment	\$ 28,030.00
2		CME OH&P 5% on INM		\$ 1,401.05
3	09-09500 - Framing/Ceilings/Tectum	Rosema - Area 1 - Remove/reinstall 1 row of ceiling tiles per row of lights for INM to service lights.	Commitment	\$ 1,045.00
4		CME OH&P 5% on Rosema		\$ 52.25
5	01-01524 - Temporary Protection - Finishe	CME - Labor	Labor	\$ 1,239.20
6	01-01524 - Temporary Protection - Finishe	CME - Materials	Materials	\$ 400.00



7	01-01524 - Temporary Protection - Finishe	CME - equipment	Equipment	\$ 300.00
8	01-01715 - Waste Disposal	CME - Other	Other	\$ 1,180.00
9	01-01011 - Project Superintendant	CME - Supervision	Labor	\$ 1,736.00
10		CME - OH&P 10% on self performed scope		\$ 485.52
11	01-01910 - P & P Bond	CME - Bond 1.5%	Other	\$ 538.04
<b>Subtotal:</b>				\$36,407.06
<b>Grand Total:</b>				<b>\$36,407.06</b>

	Rejected: Proceed per Original Contract	
	Approved to Proceed with Work: Change Order Forthcoming	
	Approved to Proceed with Work: Use Owner Contingency	
	Other: _____	
By:		Date:

CME Corporation  
7235 Vicksburg Pike  
Fort Wayne, 46804  
Phone: (260) 745-0251

**Project:** 19218 - Wells County Public Library Interior Renovation  
200 W Washington St  
Bluffton, Indiana 46714

## Prime Contract Potential Change Order #044: CE #097 - SI-15.2 - New Lighting Area 2 OF 2

<b>TO:</b>	Wells County Public Library 200 W Washington Street Bluffton Indiana, 46714	<b>FROM:</b>	CME Corporation 7235 Vicksburg Pike Fort Wayne Indiana, 46804
<b>PCO NUMBER/REVISION:</b>	044 / 0	<b>CONTRACT:</b>	1 - Wells County Public Library Interior Renovation
<b>REQUEST RECEIVED FROM:</b>	Andrew Hesterman (MKM architecture + design)	<b>CREATED BY:</b>	Sean Hayes (CME Corporation)
<b>STATUS:</b>	Pending - In Review	<b>CREATED DATE:</b>	5/8 /2020
<b>REFERENCE:</b>		<b>PRIME CONTRACT CHANGE ORDER:</b>	None
<b>FIELD CHANGE:</b>	Yes		
<b>LOCATION:</b>	127/128	<b>ACCOUNTING METHOD:</b>	Amount Based
<b>SCHEDULE IMPACT:</b>		<b>PAID IN FULL:</b>	No
		<b>TOTAL AMOUNT:</b>	\$42,910.36

**POTENTIAL CHANGE ORDER TITLE:** CE #097 - SI-15.2 - New Lighting Area 2 OF 2

**CHANGE REASON:** Client Request

**POTENTIAL CHANGE ORDER DESCRIPTION:** *(The Contract Is Changed As Follows)*

CE #097 - SI-15.2 - New Lighting Area 2 OF 2

See attached SI-15.2 - New Lighting in rooms 127/128. - **AREA 2 OF 2**

Item No. 1: On sheet E-001, the electrical contractor shall state the cost for the demolition of lighting in Children's Collection Room #147, Teen Lounge Room #129, and Collection Room #128 as shown on attached Supplemental Information Drawing 2414E001-03-25-2020-SI-15.

Item No. 2: On sheet E-201, the electrical contractor shall state the cost for the addition of new fixtures specified in Children's Collection Room #147, Teen Lounge Room #129, and Collection Room #128 as shown on attached Supplemental Information Drawing 2414E201-03-25-2020-SI-15R1a, 2414E201-03-25-2020-SI-15R1b, and 2414E201-03-25-2020-SI-15R1c. Contractor provide all hardware, accessories, conduit, and conductors for a complete and code compliant system.

This PCO excludes a new ceiling system in 127.

**ATTACHMENTS:**

[INM PR - SI 15\\_2.pdf](#) [2020-05-05\\_SI-15.2 - New Lighting - Breakdown Designations.pdf](#)

#	Cost Code	Description	Type	Amount
1	16-16050 - Basic Electrical Materials	INM - SI-15.2-Area 2 - New Lighting	Commitment	\$ 36,470.00
2		CME OH&P 5% on INM		\$ 1,823.50
3	01-01524 - Temporary Protection - Finishe	CME - Labor	Labor	\$ 1,239.20
4	01-01524 - Temporary Protection - Finishe	CME - Materials	Materials	\$ 200.00
5	01-01524 - Temporary Protection - Finishe	CME - equipment	Equipment	\$ 150.00
6	01-01715 - Waste Disposal	CME - Other	Other	\$ 1,180.00



7	01-01011 - Project Superintendent	CME - Supervision	Labor	\$ 868.00
8		CME OH&P 10% on self-performed scope		\$ 345.52
9	01-01910 - P & P Bond	CME Bond 1.5%	Other	\$ 634.14
<b>Subtotal:</b>				\$42,910.36
<b>Grand Total:</b>				<b>\$42,910.36</b>

	Rejected: Proceed per Original Contract	
	Approved to Proceed with Work: Change Order Forthcoming	
	Approved to Proceed with Work: Use Owner Contingency	
	Other: _____	
By:		Date:

**Pricing Requested****INM Electric      Resulting from SI 15.2**Project Well County Public LibraryDate 5/8/2020

The following is to be considered as a change in the scope of work and/or the specification of required material from the original design of the project listed above.

Labor and material for work needed in response to SI 15.2. New light fixtures and  
controls in rooms 127, 128, 147 and 148. Pricing includes all additional raceway and wiring  
needed for complete installation. Dumpster for removed fixtures by others

Total Cost of changes to original contract	<b>Area 1 – 147/148</b>
	Add Labor \$7100
	Add (lights) \$18,860
	Add (Controls) \$1130
	Add (wire/raceway/hardware) \$940
	<b>Total Area 1 \$28,030</b>
	<b>Area 2 – 127/128</b>
	Add Labor \$14,600
	Add (Lights) \$20,040
	Add (Controls) \$550
	Add ( wire/raceway/hardware) \$1280
	<b>Total Area 2 \$36,470</b>
	<b>Total Adder \$64,500</b>

The above changed are as a result of:

CE 80 and SI 15.1

---

---





# Rosema Corporation

FLOORS • WALLS • CEILINGS

**FORT WAYNE**  
8333 Clinton Park Drive  
Fort Wayne, IN 46825  
P 260.482.6501  
F 260.482.6510

**MUNCIE**  
411 W. Ontario Drive  
Muncie, IN 47307  
P 765.282.9404  
F 260.482.6510

**SOUTH BEND**  
3275 Elwood Avenue  
South Bend, IN 46628  
P 574.217.7700  
F 574.217.7556

May 4, 2020

CME Corporation

Attn: Sean Hayes

## Proposal for: Wells County Public Library

### RE: Revised SI-15.1

Install new ceiling tile and grid (ACP-2) in Room 127.

\*Assumes work area to be clear of shelving/bookcases. Excludes rework/reinstallation of acoustic in Rooms 128, 129, 130 and 147.

**Material: \$2,620.00**

**Labor: \$1,030.00**

**OH/P: \$365.00**

**COSTS TO BE  
SUBMITTED UNDER  
SEPARATE COVER**

~~**Total: \$4,015.00**~~

### Voluntary add:

**Remove/reinstall ceiling tiles next to lights in Room 147.**

\*Assumes all ceiling tile can be reused.

**Material: \$0.00**

**Labor: \$950.00**

**OH/P: \$95.00**

**INCLUDED IN  
SI-15.2 AREA 1  
ONLY**

**Total: \$1,045.00**

**SI-15.1 Total Add: \$5,060.00**

Respectfully submitted:

Charles Bickford

Project Manager
